ADVISORY GROUP

SCHEDULE

Bidding Process

Completed – Final material determination

Advisory Group Meeting

May 17th, 2017 First Meeting

Intergovernmental Agreement (IGA)

In Draft Form

Shovels In The Ground – June 10-12

Advisory Group Meeting


Targeting Later June To Discuss Construction Work

Planting – Mid To Late August (Weather Dependent)

Meeting With Advisory Group Prior To Planting To Confirm Actual Location

Completion – End of August


LONI - LETTER OF NO WETLAND IMPACT

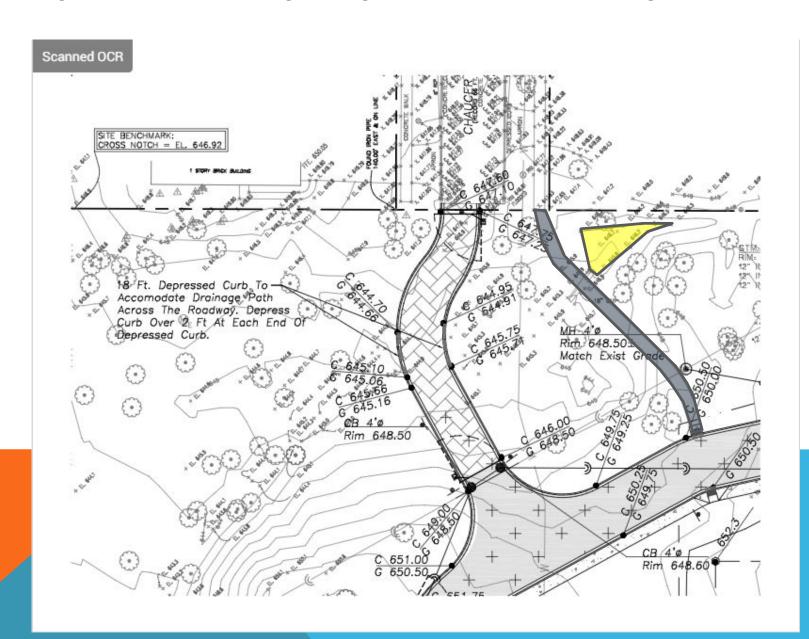


SOIL SAMPLES

- Detention System
 - Depth
 - Size
- Road Bed Foundation
- General Conditions For Normal Drainage

DRAINAGE - TODAY

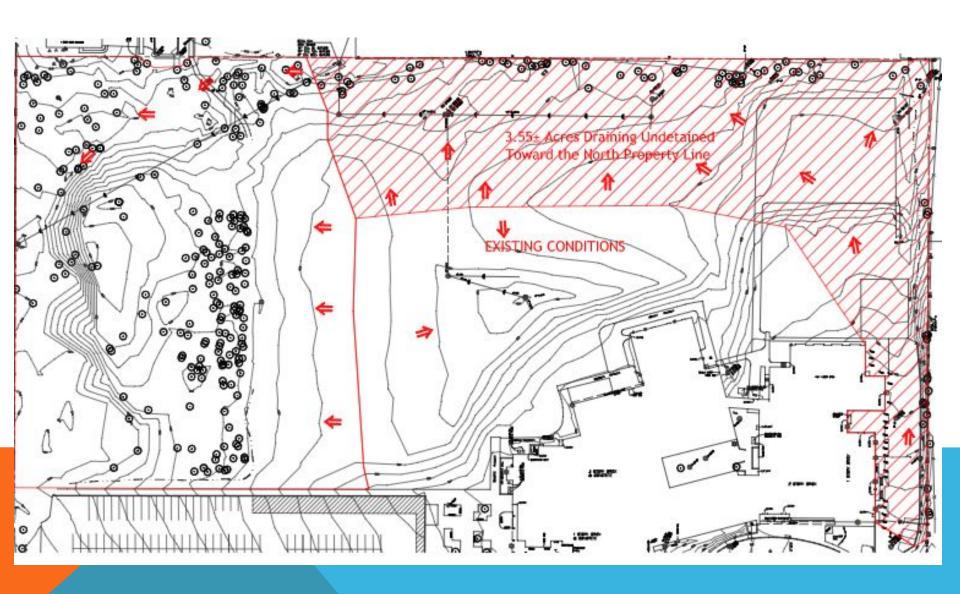

DRAINAGE - FUTURE

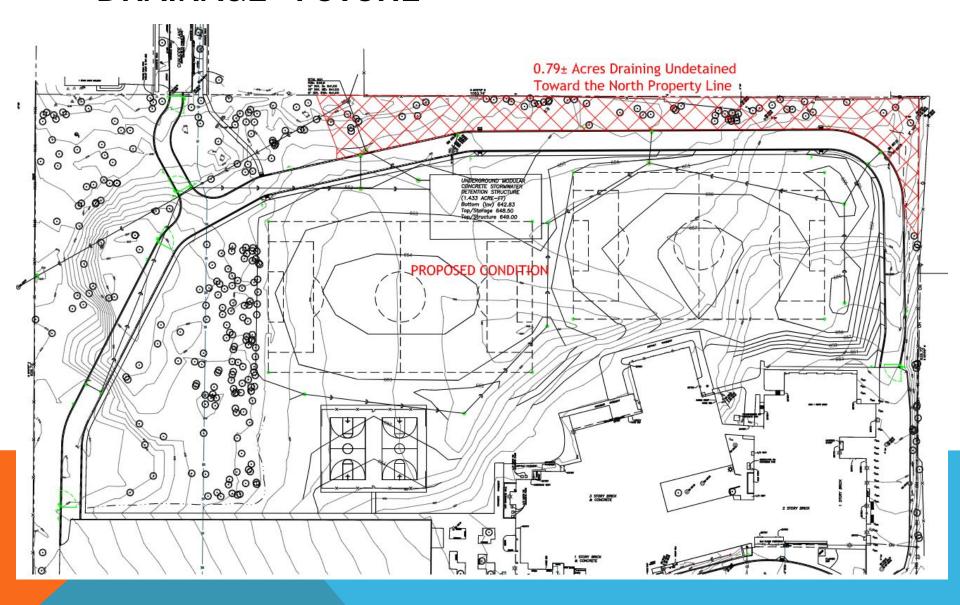



CHAUCER ROAD GATE


RENDERING OF VIEW SOUTH AT END OF CHAUCER LANE




HORTH SHORE SD 152-PLANNING AND DESIGN COMMISSION APPROVAL-POLLOW-UP MEETING-5

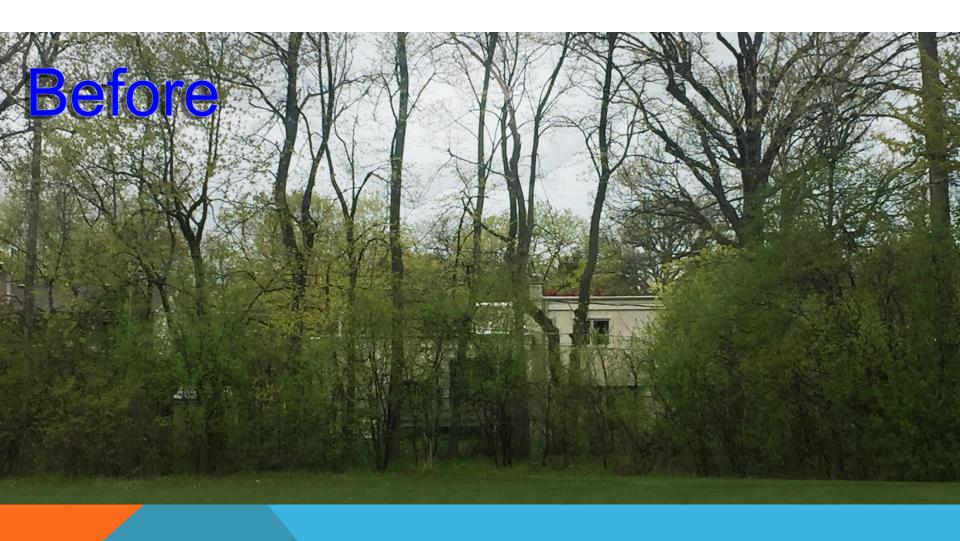

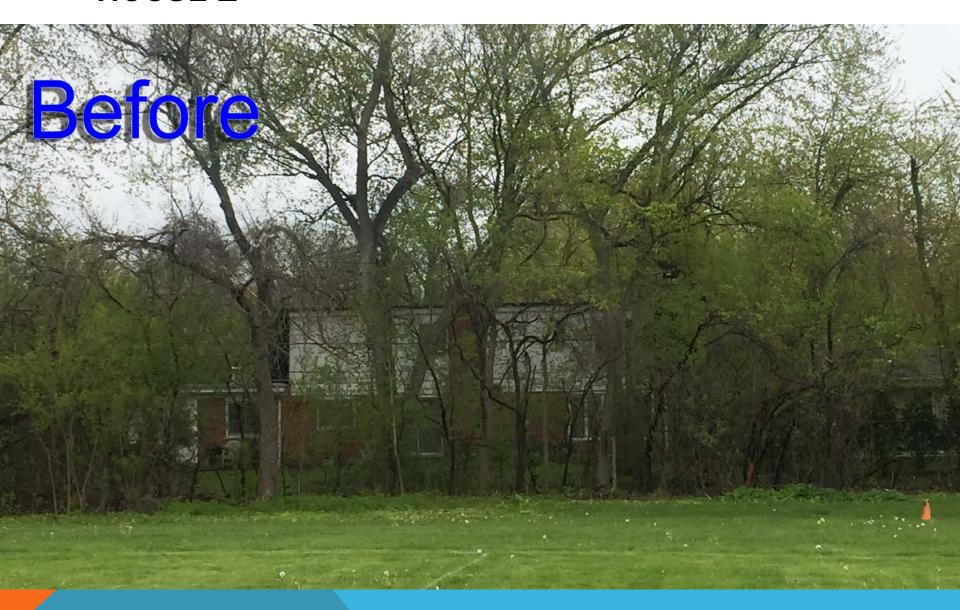

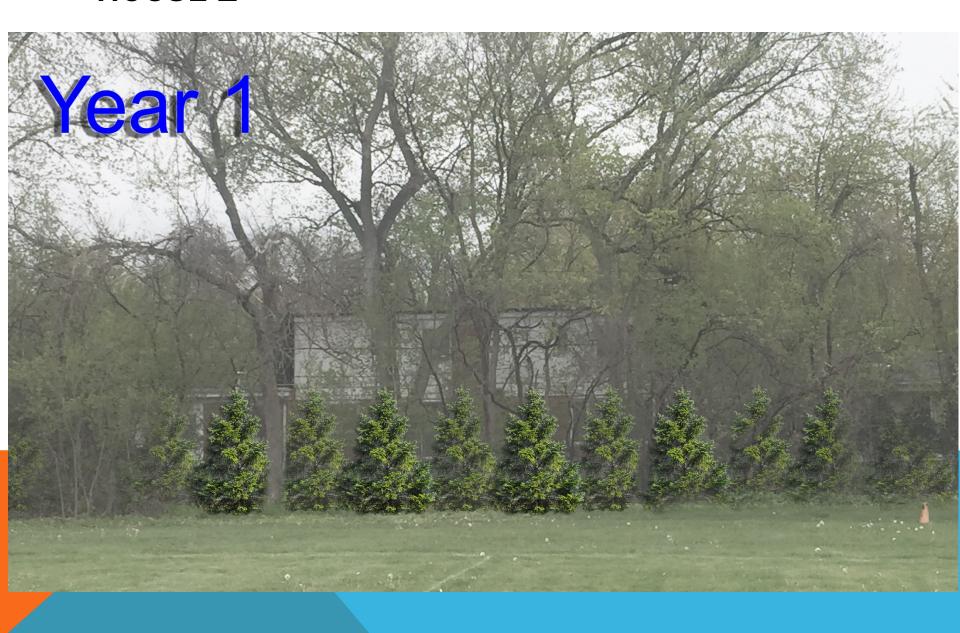

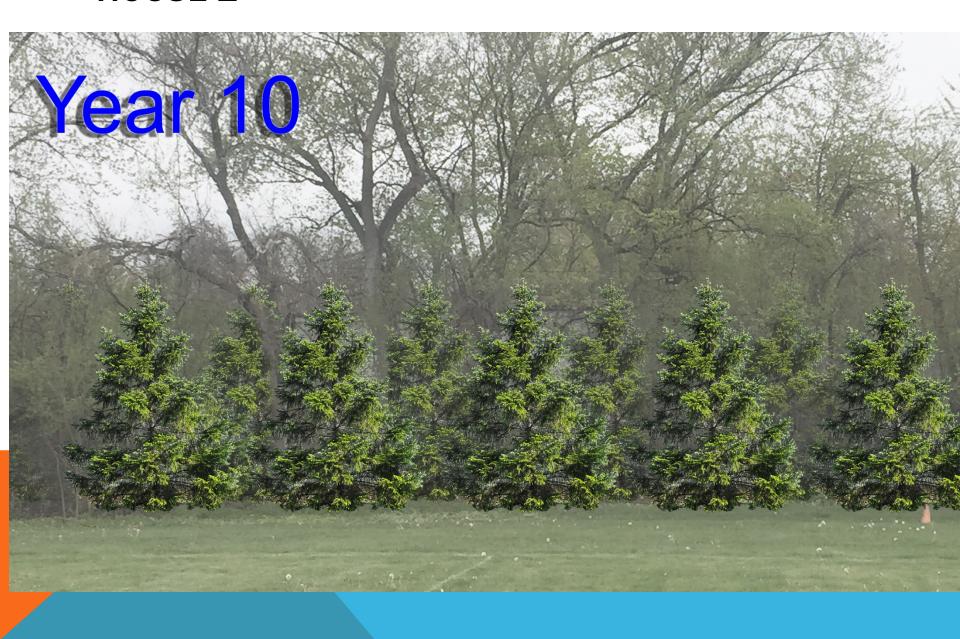

LANDSCAPE PLAN

